




CITY OF West Linn

Memorandum

TO: Transportation Advisory Board
FROM: Chris Kerr, Senior Planner
DATE: October 21, 2009
SUBJECT: Updated transit shelter implementation timeline

This memo provides a summary of the major project tasks and an approximate implementation schedule for providing three (3) transit shelters along OR 43. Below is a general timeline to install these shelters.

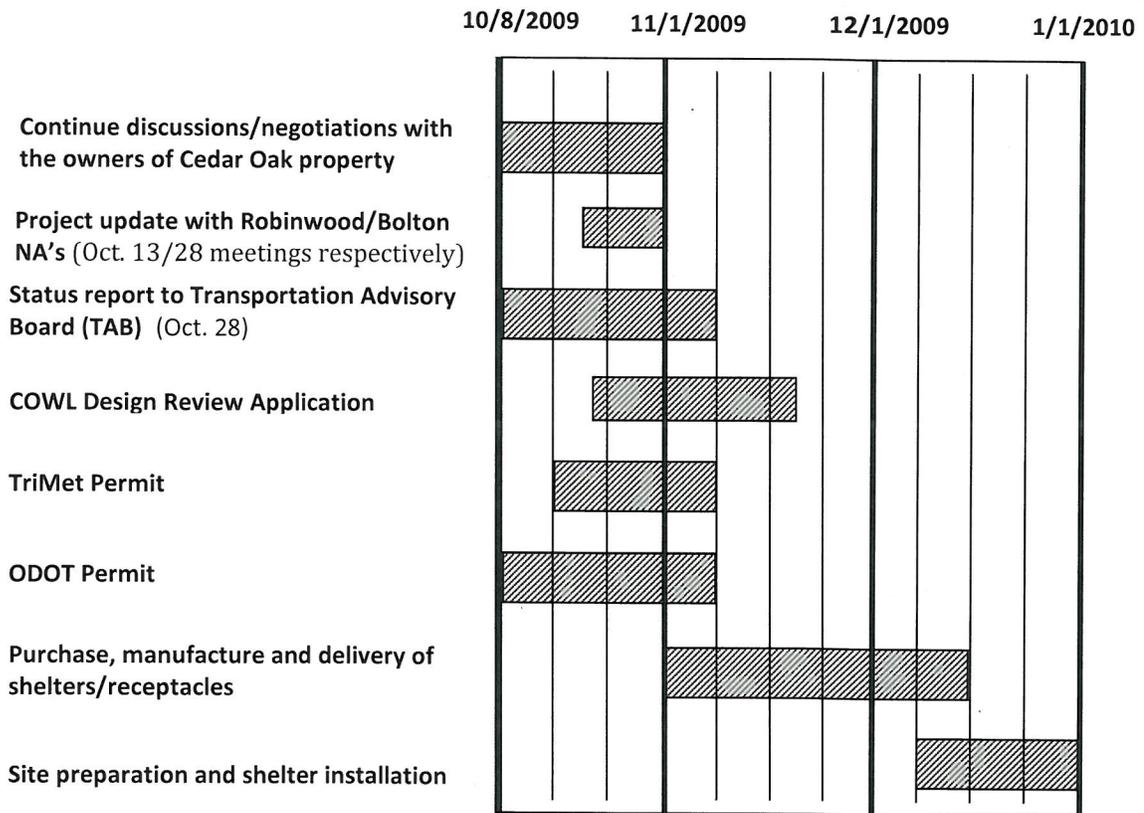

Presently, assuming that that we can address the site constraints at the Cedar Oak shelter location (via easement or alternate shelter design) and provided no new unexpected permitting issues arise, we anticipate having the shelters installed prior to December 31, 2009. Currently, Staff anticipates purchasing, processing and installing all three (3) shelters simultaneously; however, if it becomes apparent that the site constraints at the Cedar Oak site will require additional time to resolve, Staff will process and install the other two shelters separately.
