CITY OF WEST LINN PUBLIC IMPROVEMENT PROJECT

CITY OF West Linn

PUBLIC WORKS DEPARTMENT - ENGINEERING DIVISION

Public Works Director: Lance Calvert, P.E.
Phone: 503-722-5500
Fax: 503-656-4106
http://www.westlinnoregon.gov/publicworks

Median Restoration Project

Project Number: PW-13-13

TEAM

CITY

Department: Streets
City's Project Manager: Jeff Randall/Streets Supervisor
Contact Number: 503-742-8616

CONSULTANT

Design Consultant: Walker Macy

CONTRACTOR

General Contractor: N/A
Program Manager:
Contact Number:

PROJECT DESCRIPTION

This is an in-house project involving the coordination of the Street and Parks Department and includes the removal of all existing vegatation within designated medians as well as approximately 800 cubic yards of dirt. The City of West Linn will lay approximately 800 cubic yards of a 3-way blended soil, replant the islands with trees and bushes then add a layer of bark dust. The city is working with a landscape consultant to design the layout and overall appearance of the islands.

Design and Plans

SCHEDULE

PROJECT PHASES	Percent Completed	Original Estimated Completion Date	Projected Completion Date
Consultant Selection	100%		
Design Completion	75%	Nov-13	
Const Contract Award	N/A		
Const Completion	30%	Dec-13	
Total Project Completion:	30%		

PROJECT STATUS

Plants, trees, vegetation and 12" of dirt has been removed majority of the islands. 12" of 3way blended soil has been laid and new trees have been planted. Total project is 75% completed



PROJECT BUDGET

	BUDGET
Original	$ 50,000
Amendment(s)	$ -
Revised	$ -

	BUDGET	ACTUAL
FY11-12	$ -	$ -
FY12-13	$ -	$ -
FY13-14	$ 50,000	$ -

DETAIL

	BUDGET	ACTUAL
Design	$ -	$ -
R/W - Land	$ -	$ -
Construction	$ 50,000	$ -
Total Expended		**$ -**

PROJECT PHOTOS

DESIGN EXAMPLE

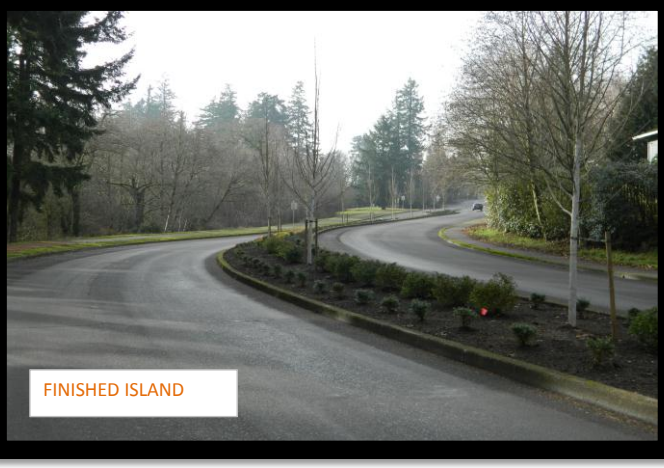
FINISHED ISLAND

Last Updated : 1/02/2014
